



Felicity Adobe

Happy homes for all



Homes for all

Swarna Griha – 3 | Serene Highlands

Progress Report of Month October 2023



REDMI NOTE 11

04/11/2023 15:33

SWARNAGRIHA 03 – SERENE HIGHLANDS

PROJECT INFORMATION

- 1. Project Name : Swarna Griha - 03.**
- 2. Building : 4 Towers (A,B,C&D) of Basement + Ground + 12 Floors.**
- 3. Flats in Each Tower : 130nos 2BHK.**
- 4. Total no. of Flats : 520nos 2BHK.**
- 5. Site Area : 9387.6 SQ M**
- 6. Total BUA : 3,66,566 SQ ft.**
- 7. FAR : 3**
- 8. Area per Unit : 46.68 SQ M**
- 9. Car park provided : 264nos**

CONSULTANT DETAILS

- Developer : **FELICITY ADOBE LLP**
- Project name : **Swarna Griha 03**
- Architect : **Cast Studios**
- Structural consultant : **Rajesh Consultants**
- Services
 - Plumbing and Fire : **Vruddhi Associates**
 - Electrical : **Design Analysis**


SG03 – PROGRESS TREE

TOWER B	TOWER A	TOWER C
	TERRACE FLOOR - 02.02.2023	TERRACE FLOOR
12 th FLOOR IN PROGRESS	12th FLOOR - 17.01.2023	12th FLOOR
11 TH FLOOR – 20.10.2023	11th FLOOR - 26.12.2022	11th FLOOR
10 TH FLOOR – 23.09.2023	10th FLOOR - 17.12.2022	10th FLOOR
9 th FLOOR – 31.08.2023	9th FLOOR - 03.12.2022	9th FLOOR
8 TH FLOOR – 12.08.2023	8th FLOOR - 23.11.2022	8th FLOOR
7 TH FLOOR – 19.07.2023	7th FLOOR - 10.11.2022	7th FLOOR
6 th FLOOR - 30.06.2023	6th FLOOR - 29.10.2022	6th FLOOR
5th FLOOR – 17.06.2023	5th FLOOR - 18.10.2022	5th FLOOR
4th FLOOR – 29.05.2023	4th FLOOR -06.10.2022	4th FLOOR
3 RD FLOOR – 16.05.2023	3rd FLOOR -24.09.2022	3rd FLOOR
2 ND FLOOR – 28.05.2023	2ND FLOOR - 08.09.2022	2ND FLOOR
1 ST FLOOR – 12.05.2023	1ST FLOOR -26.08.2022	1ST FLOOR
GROUND FLOOR -18.03.2023	GROUND FLOOR -11.08.2022	GROUND FLOOR
BASEMENT FLOOR		

Completed

Progress

MASTER PLAN

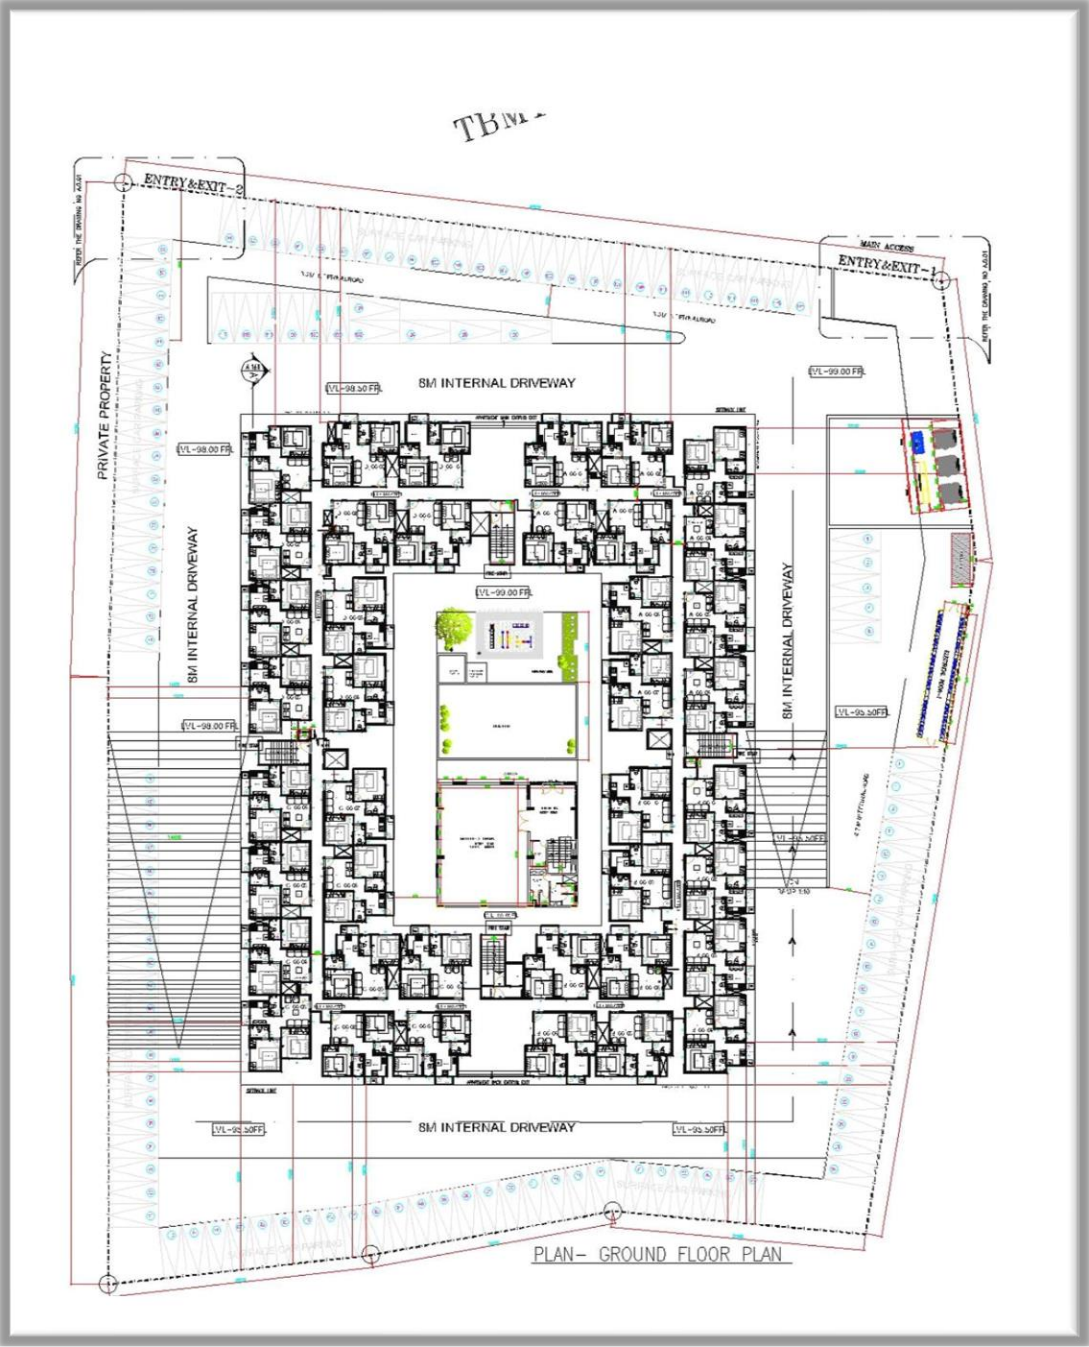

PROGRESS PHOTOS



BEFORE



PRESENT

TOWER B CONSTRUCTION PROGRESS COMPARISON



REDMI NOTE 11

04/11/2023 15:41

BEDWI NOTE 11

04/11/2023 15:41

TOWER C WEST SIDE ELEVATION



REDMI NOTE 11

04/11/2023 15:37

REDMI NOTE 11

04/11/2023 15:37

TOWER C SOUTH SIDE ELEVATION



REDMI NOTE 11

04/11/2023 15:33

REDMI NOTE 11

04/11/2023 15:33

TOWER C NORTH SIDE ELEVATION



REDMI NOTE 11

04/11/2023 15:44

REDMI NOTE 11

04/11/2023 15:44

TOWER C EAST SIDE ELEVATION

TOWER B 12th FLOOR UNITS SHUTTERING WORK IN PROGRESS



BEFORE



PRESENT

CLUB HOUSE SHUTTERING WORK IN PROGRESS



REDMI NOTE 11

03/11/2023 10:27

REDMI NOTE 11

03/11/2023 10:53

Tower B 12TH floor shuttering & wall reinforcement works in progress





BEFORE



PRESENT

TOWER C UNITS CP & SANITARY FIXING WORKS IN PROGRESS







Basement floor ceiling painting work in progress

Tower A internal toilets dado fixing work at 2nd floor in progress



Tower A internal units putty work & Sanding work in progress

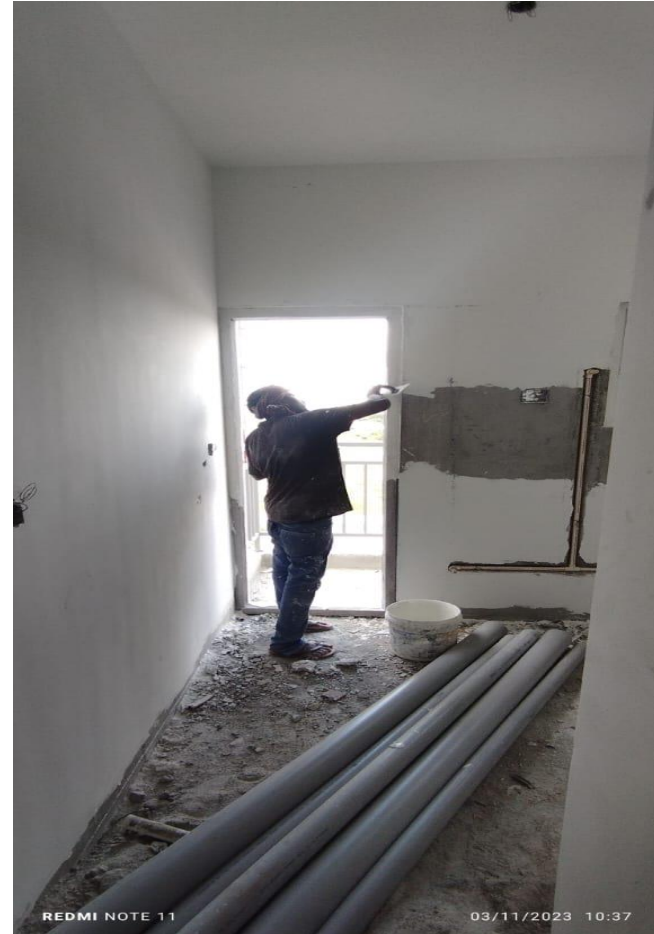



Felicity Adobe

Happy homes for all

THANK YOU

Happy homes for all
